



La Brea LCW-1 Updates

Public Works Commission Meeting

August 11, 2022



LCW-1 Equipping



Interior Piping




LCW-1 Equipping



Interior Piping and Electrical



LCW-1 Equipping

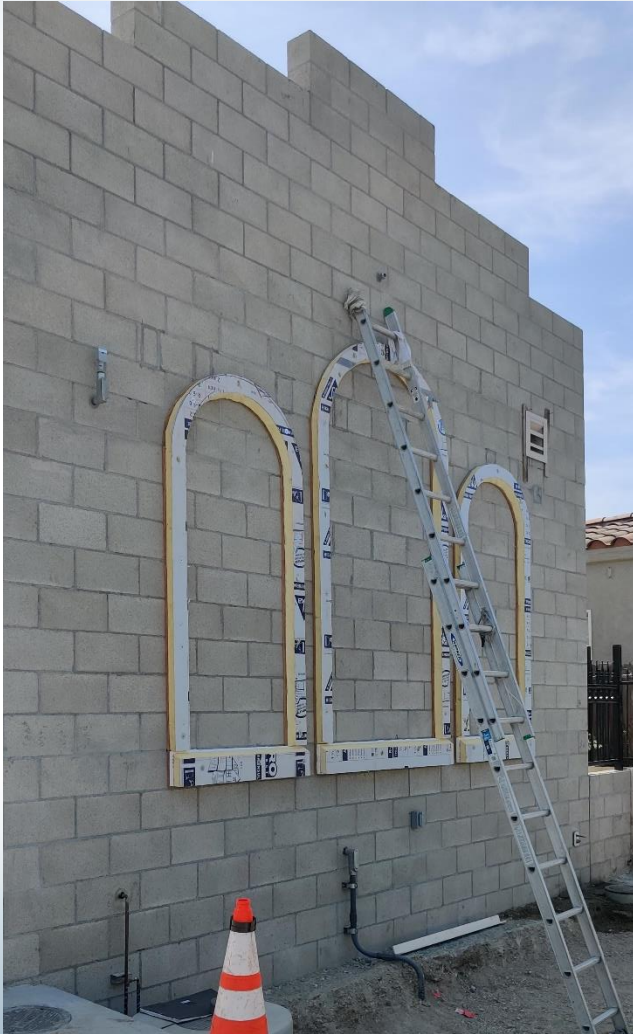

Building Exterior and Perimeter Fencing



LCW-1 Equipping



Parking Lot



La Brea Subarea Overview

LCW NO. 1 – EQUIPPING


- Budget: \$2,900,000
- Work Billed: \$2,461,507
- Percent Work Complete: 91%

SAND PIT – Nested Monitoring Well

- Budget: \$884,276
- Work Billed: \$797,625
- Percent Work Completed: 100%
- Test results under review



La Brea Subarea Development Project Timeline

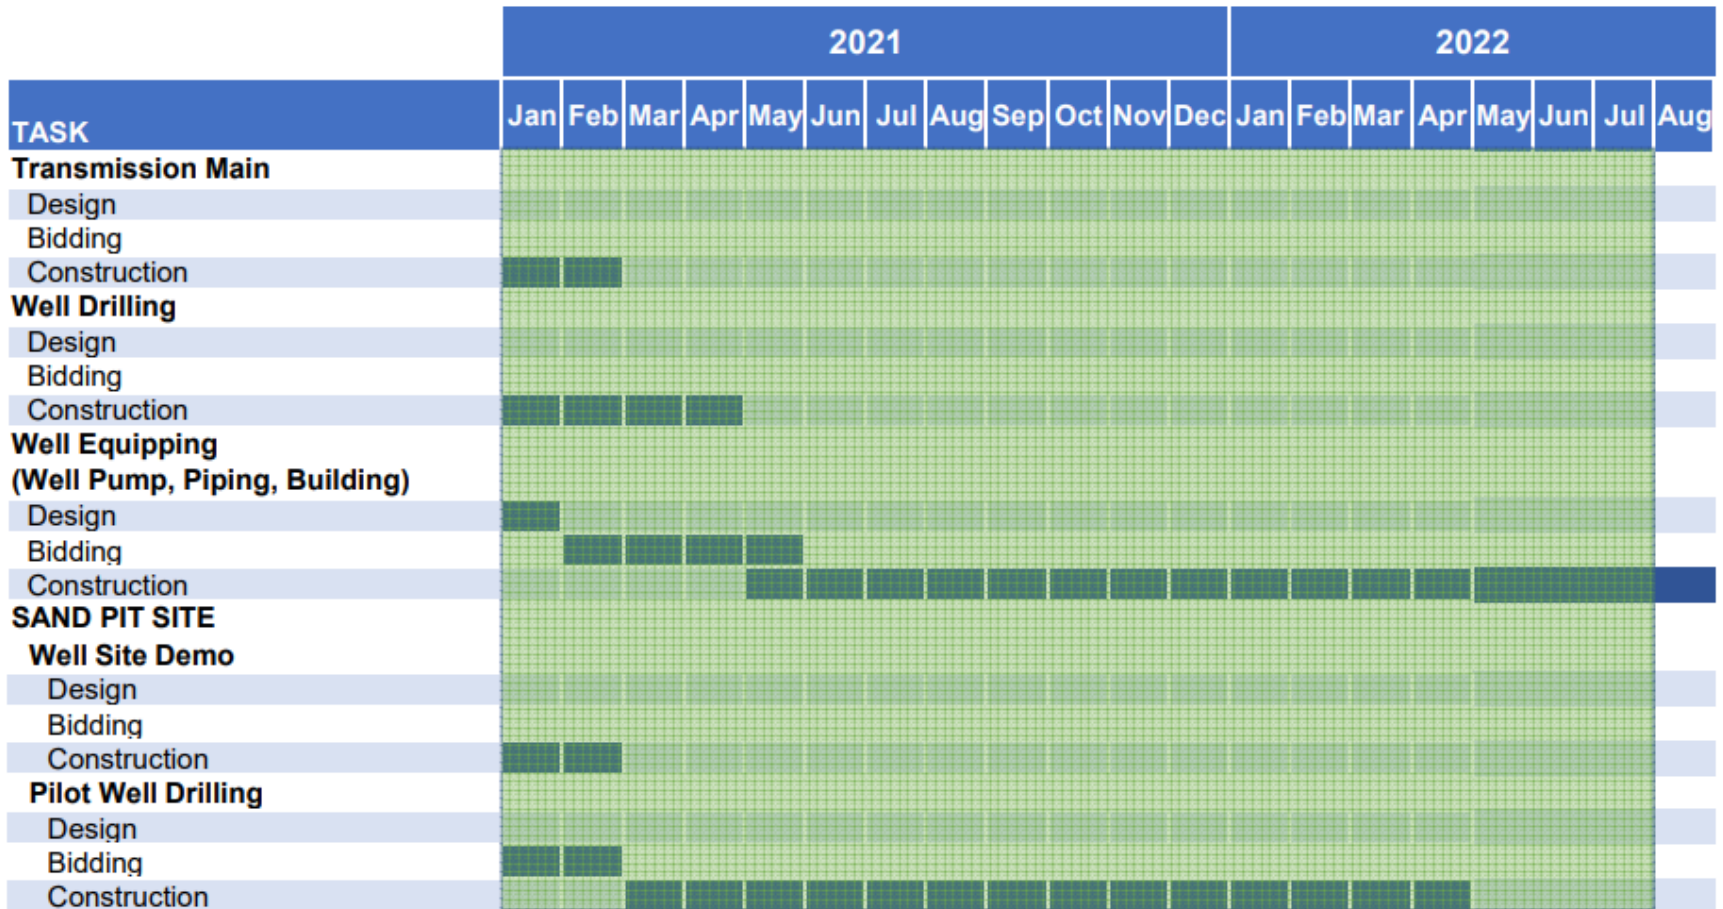

Legend
 Task Duration

Project Progress
