



# La Brea LCW-1 Updates

Public Works Commission Meeting

July 21, 2022



# LCW-1 Equipping



Interior Piping and Electrical



# LCW-1 Equipping



Exterior Wall and Bladder Surge Tank



# LCW-1 Equipping



Parking Lot



## La Brea Subarea Overview

### LCW NO. 1 – EQUIPPING

- Budget: \$2,900,000
- Work Billed: \$2,246,872
- Percent Work Complete: 85%


### SAND PIT – Nested Monitoring Well

- Budget: \$884,276
- Work Billed: \$797,625
- Percent Work Completed: 100%
- Test results pending



# La Brea Subarea Development Project Timeline

**Beverly Hills La Brea Subarea - La Cienega Well No. 1, Transmission Main, and Sand Pit Site  
Project Timeline July 2022**

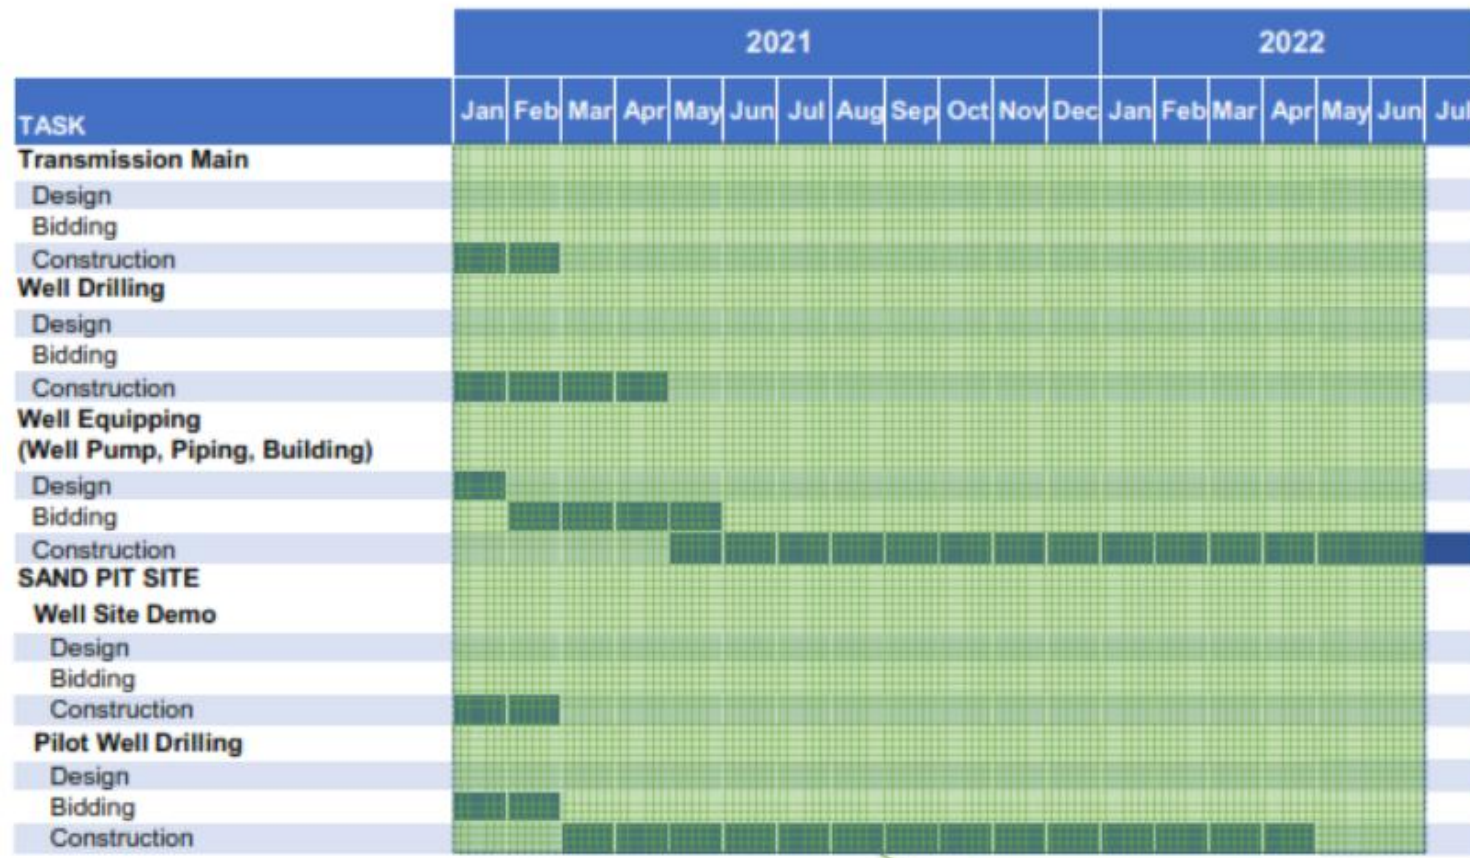

**Legend**  
 Task Duration  
 Project Progress
