



La Brea LCW-1 and Sand Pit Sites Updates

Public Works Commission

April 14, 2022




LCW-1 Equipping



Frame, Doors & Windows




LCW-1 Equipping

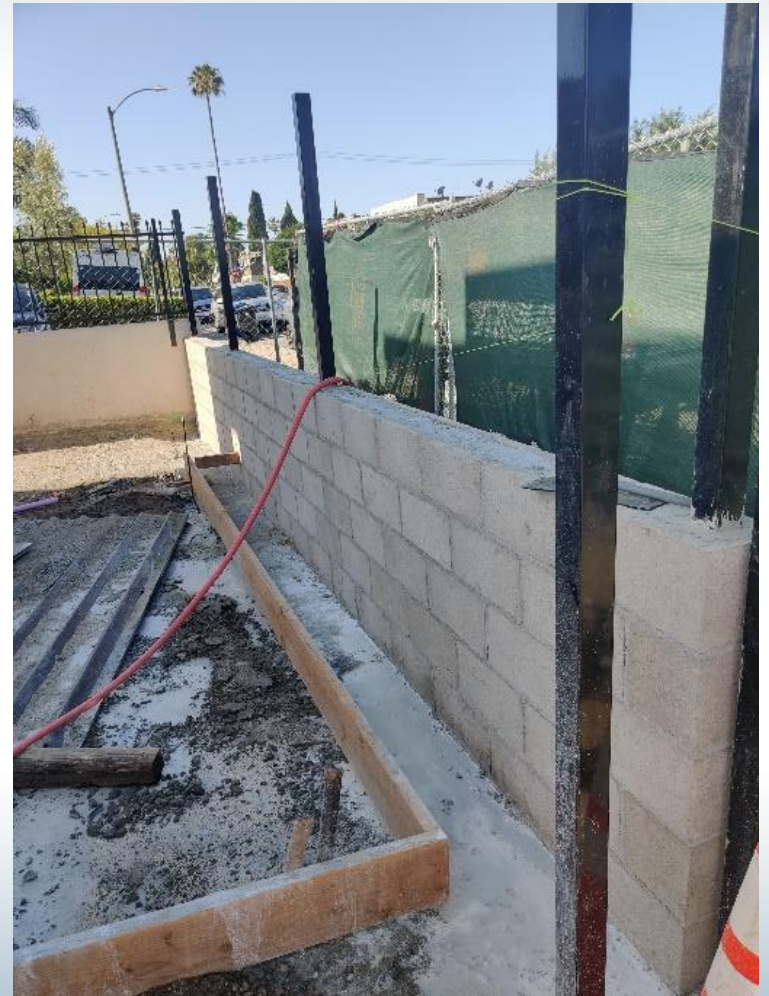

Interior Pads & Perimeter Fencing



LCW-1 Equipping

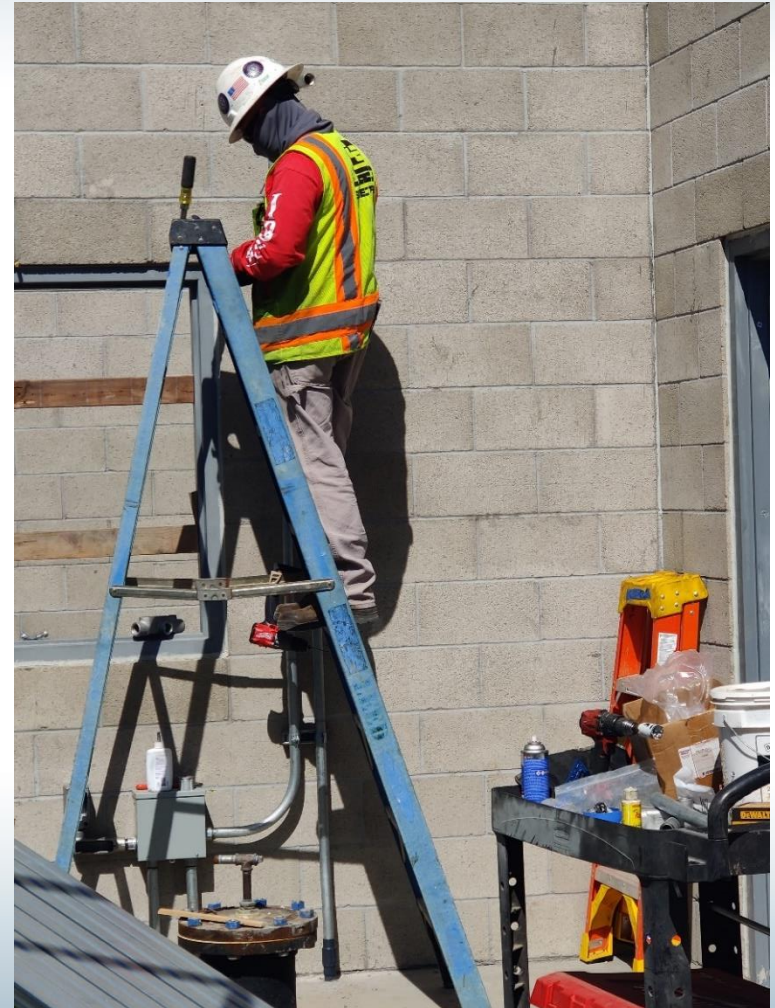

Electrical Work



Nested Monitoring Well (Sand Pit)



Sound Wall Removal
& Site Clean-up



La Brea Subarea Overview

LCW NO. 1 – EQUIPPING

- Budget: \$2,900,000
- Work Billed: \$1,560,622
- Percent Work Complete: 60%

SAND PIT – Nested Monitoring Well

- Budget: \$884,276
- Work Billed: \$776,025
- Percent Work Completed: 95%



La Brea Subarea Development Project Timeline

